

Lab 2 — Sprint Reflection

Name: Omkar


SRN: PES1UG24CS310

Semester: V | Section: 5F


Project: Academic Elective Bidding & Allocation System (Jira project: Elective-Bidding)

Screenshots


1. Backlog: Epics and User Stories

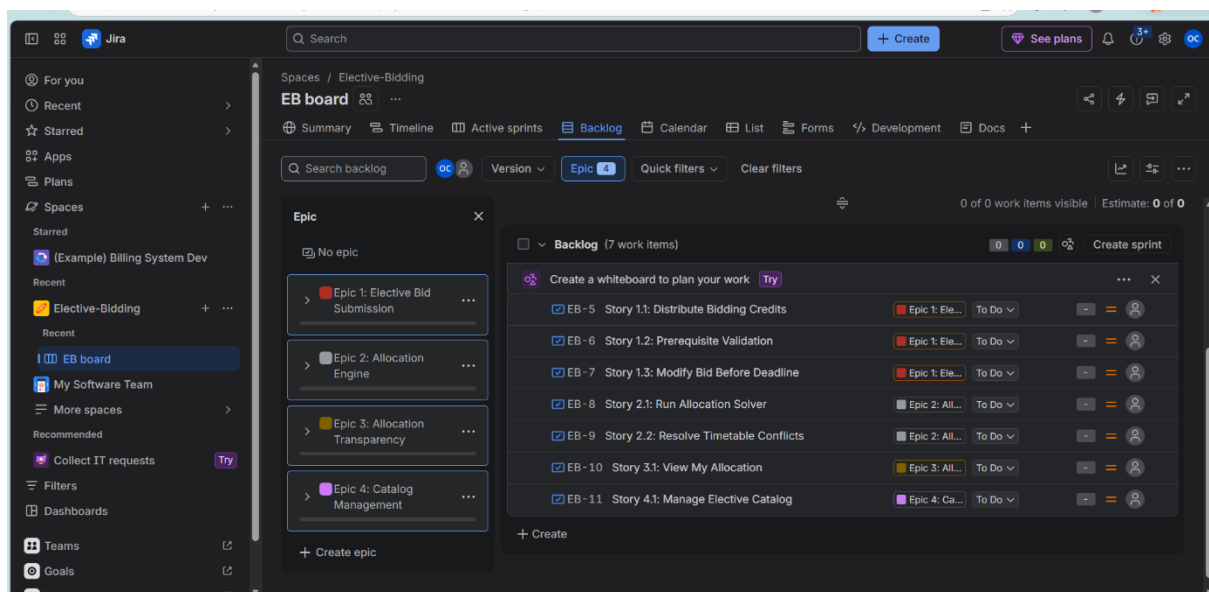

2 . Story Point Assignments

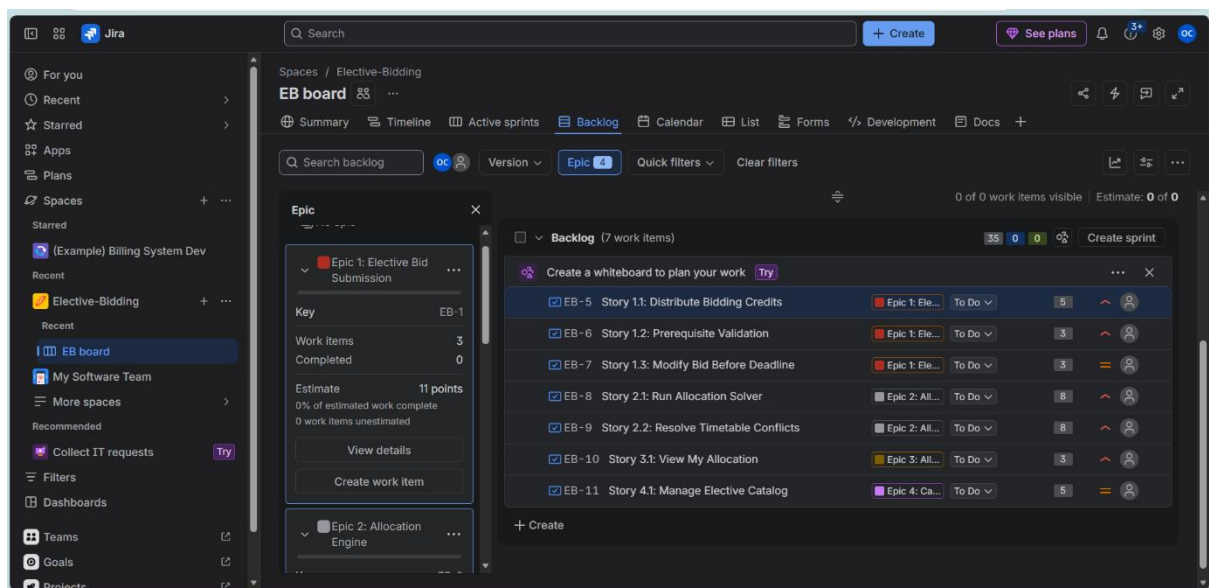

3 . Sprint Execution

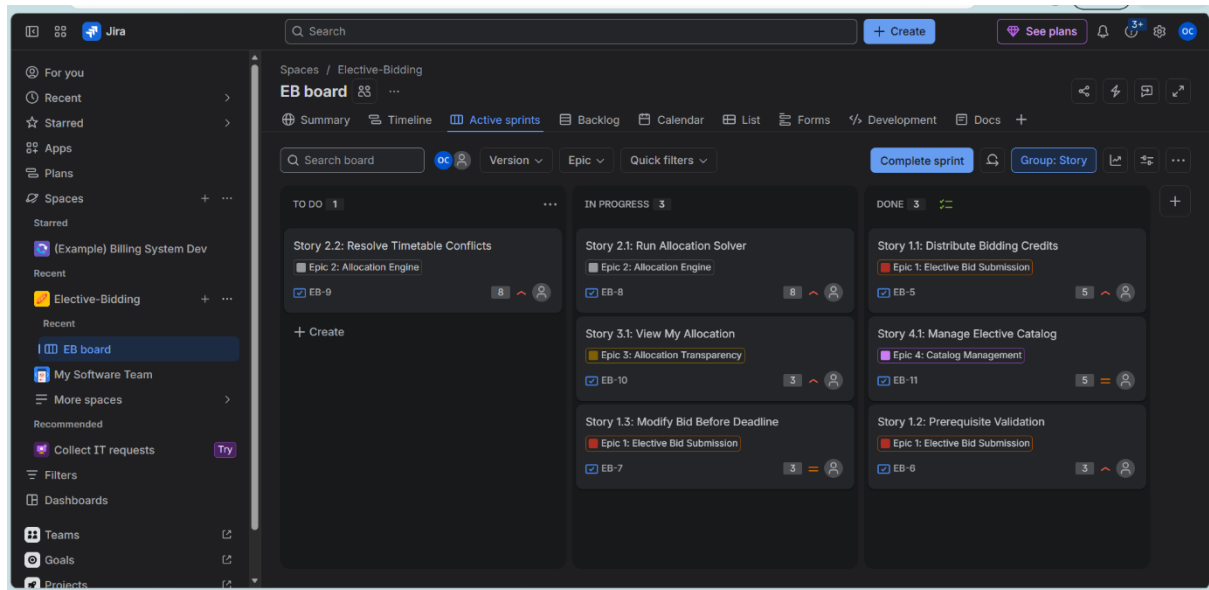

4. Burndown Chart



Reflection Questions

1. Did your estimations reflect the actual effort?

Your answer: Largely yes. The higher-point stories — EB-8 (Run Allocation Solver, 8 pts) and EB-9 (Resolve Timetable Conflicts, 8 pts) — stayed in "In Progress" across multiple check-ins while the 3-point stories (Prerequisite Validation, View My Allocation, Modify Bid) moved to Done quickly. That's consistent with the point values: the two 8-pointers represent genuinely more complex, algorithm-heavy work (constraint solving, conflict detection), so it makes sense they lingered longest on the board.

2. Was your backlog well-prioritized?

Your answer: Mostly, but one thing stands out: EB-11 (Manage Elective Catalog) was tagged Medium priority, yet it was one of the first two stories completed — which makes sense in hindsight, since the catalog has to exist before any student can bid on electives. If redoing this, Catalog Management probably deserved High priority as a blocking dependency, even though its user-facing impact felt secondary.

3. How did your simulated sprint align with your plan?

Your answer: The original plan was to split the 7 stories across two sprints, but since the professor asked for a single sprint, all 35 points went into one sprint instead. Despite that scope increase, the burndown chart shows all work reached Done by Sep 8 — well inside the 1-week window (Sep 5–Sep 11) that was set when the sprint started. So the sprint finished roughly 3 days ahead of its planned end date.

4. What insights did the burndown chart give about your team's capacity?

Your answer: The chart shows a stepped decline — 35 → 25 → 15 → 0 points — completing in about 4 days rather than the full 7. The red "remaining work" line drops well below the grey guideline early and stays there, meaning the team (in this case, one person driving the whole backlog) had more capacity than the sprint length assumed. That's a useful signal: either the 1-week duration was oversized for a 35-point backlog, or a real team could safely pull in more work next time without risking the sprint goal.
